


Skagit County - propose schedules with RCO (11 culverts design completed by 2025)

ID	Task Name	Duration	Start	Finish	Predecessors	Notes	if 1, 20 M M J S N	Half 2, 20 J M M J S N	Half 1, 20 J M M J S N	Half 2, 20 J M M J S N	Half 1, 20 J M M J S N	Half 2, 20 J M M J S N	Half 1, 20 J M M J S N
0	11 culverts project schedule	923 days	Wed 05/04/22	Fri 11/14/25		All 11 culverts MUST complete design by 2025							
1	Bring consultant onboard	49 days	Wed 05/04/22	Mon 07/11/22									
2	Advertisement - Call of Qualification	3 wks	Wed 05/04/22	Tue 05/24/22									
3	schedule for interview and selection	2.5 wks	Wed 05/25/22	Fri 06/10/22	2								
4	signed contract with Consultant	2.5 wks	Fri 06/10/22	Tue 06/28/22	3								
5	signed contract with RCO	0 wks	Tue 07/05/22	Tue 07/05/22									
6	Notice to Proceed (to consultant)	1 wk	Tue 07/05/22	Mon 07/11/22	4,5								
7	Group 1 - Culverts (2023)	200 days	Tue 07/12/22	Mon 04/17/23									
8	S. Skagit Hwy - Gilligan Creek (GN 18)	200 days	Tue 07/12/22	Mon 04/17/23	6	(48.48553, -122.13554)							
9	30% Conceptual Plans	2 mons	Tue 07/12/22	Mon 09/05/22	6								
10	30% Review; provide comments	2 wks	Tue 09/06/22	Mon 09/19/22	9								
11	60% Plans & Specs	3 mons	Tue 09/20/22	Mon 12/12/22	10								
12	60% Review; provide comments	3 wks	Tue 12/13/22	Mon 01/02/23	11								
13	90% Plans & Specs	3 mons	Tue 01/03/23	Mon 03/27/23	12	Apply for Surf Board Grant in march using 90% plans; also apply for Garden of Edens							
14	90% Review; provide comments	3 wks	Tue 03/28/23	Mon 04/17/23	13								

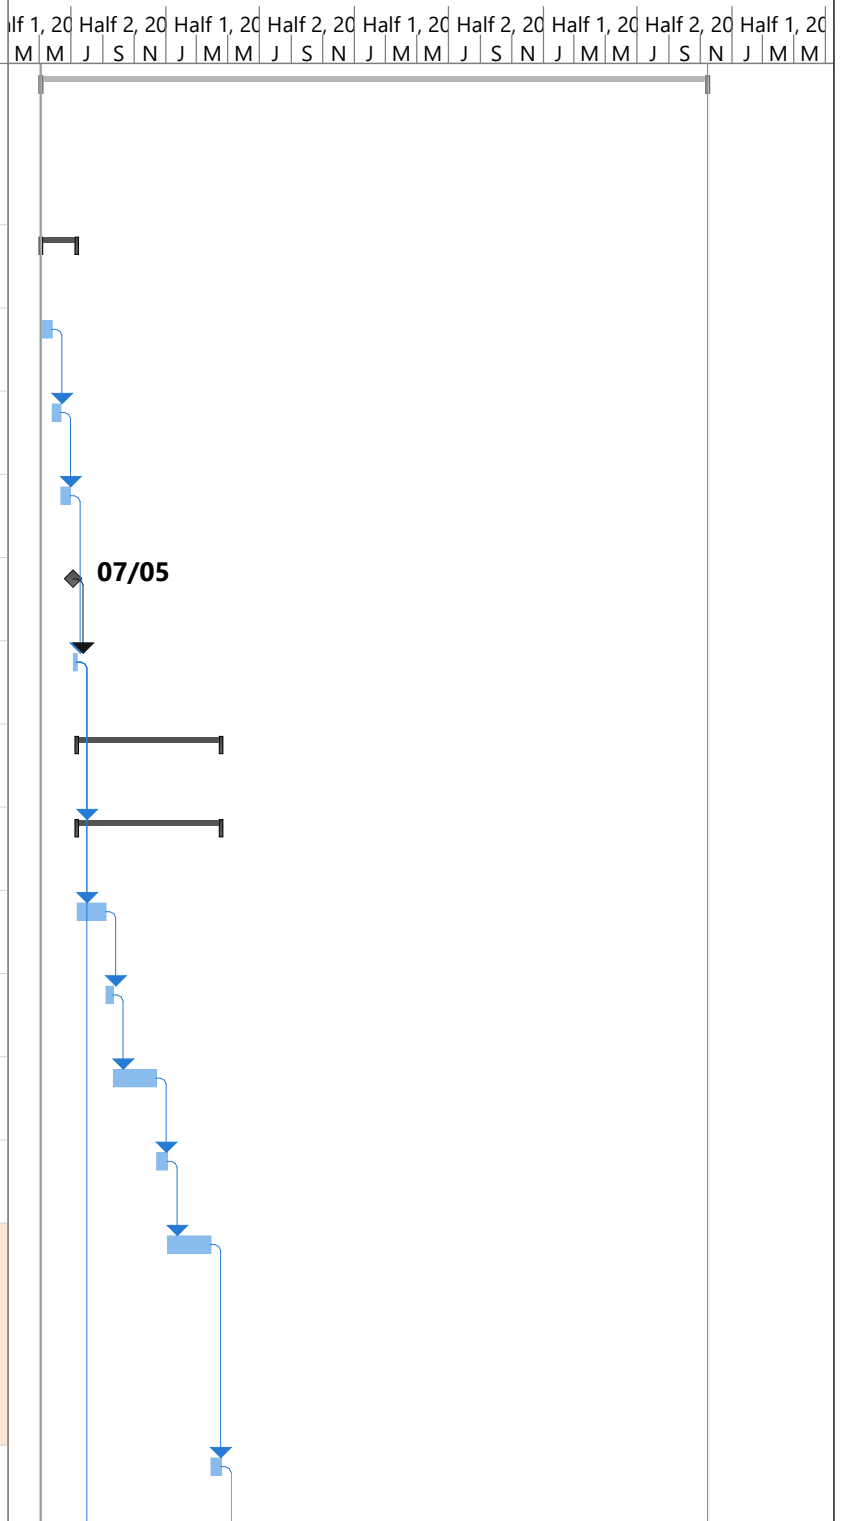


Project: 11 culverts project sche
Date: Wed 05/04/22

Task		Project Summary		Manual Task		Start-only		External Tasks		External Milestone		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Manual Progress					
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress					
Summary		Inactive Summary		Manual Summary		External Milestone							

Skagit County - propose schedules with RCO (11 culverts design completed by 2025)

ID	Task Name	Duration	Start	Finish	Predecessors	Notes	if 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	
							M	M	J	S	N	J	M	M	J	S	N	J
15	Apply for Grant	0 mons	Mon 04/17/23	Mon 04/17/23	14													
16	S. Skagit Hwy - Sorenson Creek (GN 16)	200 days	Tue 07/12/22	Mon 04/17/23	6	(48.48858, -122.10462)												
17	30% Plans	2 mons	Tue 07/12/22	Mon 09/05/22														
18	30% Review; provide comments	2 wks	Tue 09/06/22	Mon 09/19/22	17													
19	60% Plans & Specs	3 mons	Tue 09/20/22	Mon 12/12/22	18													
20	60% Review; provide comments	3 wks	Tue 12/13/22	Mon 01/02/23	19													
21	90% Plans & Specs	3 mons	Tue 01/03/23	Mon 03/27/23	20	Apply for Surf Board Grant in march using 90% plans; also apply for Garden of Edens												
22	90% Review; provide comments	3 wks	Tue 03/28/23	Mon 04/17/23	21													
23	Apply for Grant	0 mons	Mon 04/17/23	Mon 04/17/23	22	Apply for Surf Board Grant												
24	Group 2 - Culverts (2024)	279 days	Tue 04/18/23	Fri 05/10/24														
25	Friday Creek Rd - Butler Creek (FR 13)	220 days	Tue 04/18/23	Mon 02/19/24		(48.59561, -122.32834)												
26	30% Plans	3 mons	Tue 04/18/23	Mon 07/10/23	23													
27	30% Review; provide comments	2 wks	Tue 07/11/23	Mon 07/24/23	26													
28	60% Plans & Specs	3 mons	Tue 07/25/23	Mon 10/16/23	27													
29	60% Review; provide comments	3 wks	Tue 10/17/23	Mon 11/06/23	28													
30	90% Plans & Specs	3 mons	Tue 11/07/23	Mon 01/29/24	29													

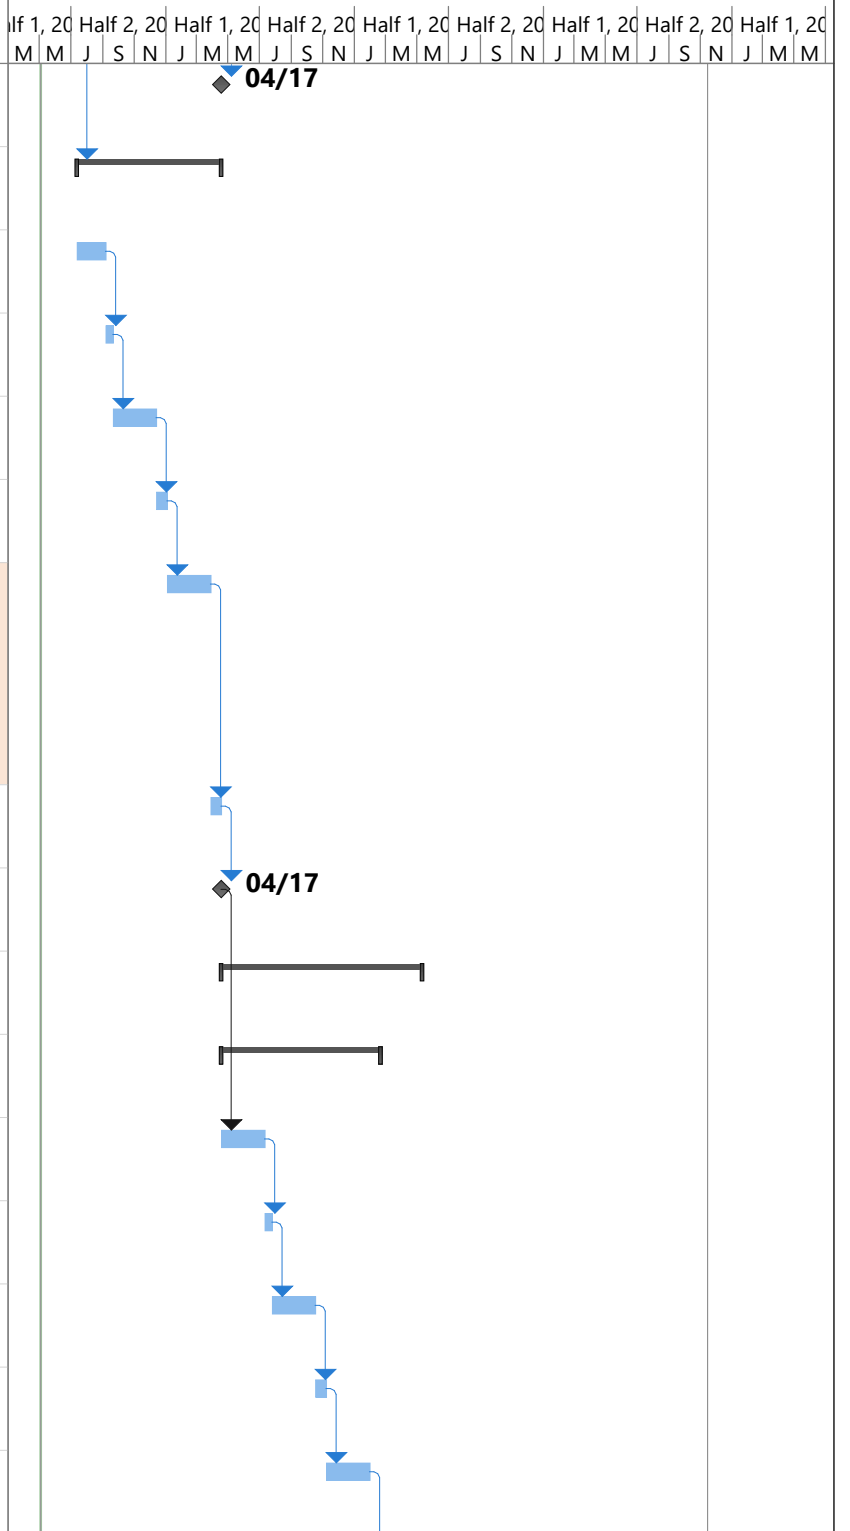


Project: 11 culverts project sche
Date: Wed 05/04/22

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Skagit County - propose schedules with RCO (11 culverts design completed by 2025)

ID	Task Name	Duration	Start	Finish	Predecessors	Notes	if 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	
							M	M	J	S	N	J	M	M	J	S	N
31	90% Review; provide comments	3 wks	Tue 01/30/24	Mon 02/19/24	30												
32	Apply for Grant	0 mons	Mon 02/19/24	Mon 02/19/24	31	FBRB											
33	Old Hwy 99 - Butler Creek (FR 14)	220 days	Mon 05/15/23	Fri 03/15/24		(48.59445, -122.3241)											
34	30% Plans	3 mons	Mon 05/15/23	Fri 08/04/23													
35	30% Review; provide comments	2 wks	Mon 08/07/23	Fri 08/18/23	34												
36	60% Plans & Specs	3 mons	Mon 08/21/23	Fri 11/10/23	35												
37	60% Review; provide comments	3 wks	Mon 11/13/23	Fri 12/01/23	36												
38	90% Plans & Specs	3 mons	Mon 12/04/23	Fri 02/23/24	37												
39	90% Review; provide comments	3 wks	Mon 02/26/24	Fri 03/15/24	38												
40	Apply for Grant	0 mons	Fri 03/15/24	Fri 03/15/24	39												
41	S. Skagit Hwy - Stevens Creek (GN 19)	220 days	Mon 06/12/23	Fri 04/12/24		(48.48426, -122.13885)											
42	30% Plans	3 mons	Mon 06/12/23	Fri 09/01/23													
43	30% Review; provide comments	2 wks	Mon 09/04/23	Fri 09/15/23	42												
44	60% Plans & Specs	3 mons	Mon 09/18/23	Fri 12/08/23	43												
45	60% Review; provide comments	3 wks	Mon 12/11/23	Fri 12/29/23	44												
46	90% Plans & Specs	3 mons	Mon 01/01/24	Fri 03/22/24	45												
47	90% Review; provide comments	3 wks	Mon 03/25/24	Fri 04/12/24	46												
48	Apply for Grant	0 mons	Fri 04/12/24	Fri 04/12/24	47												

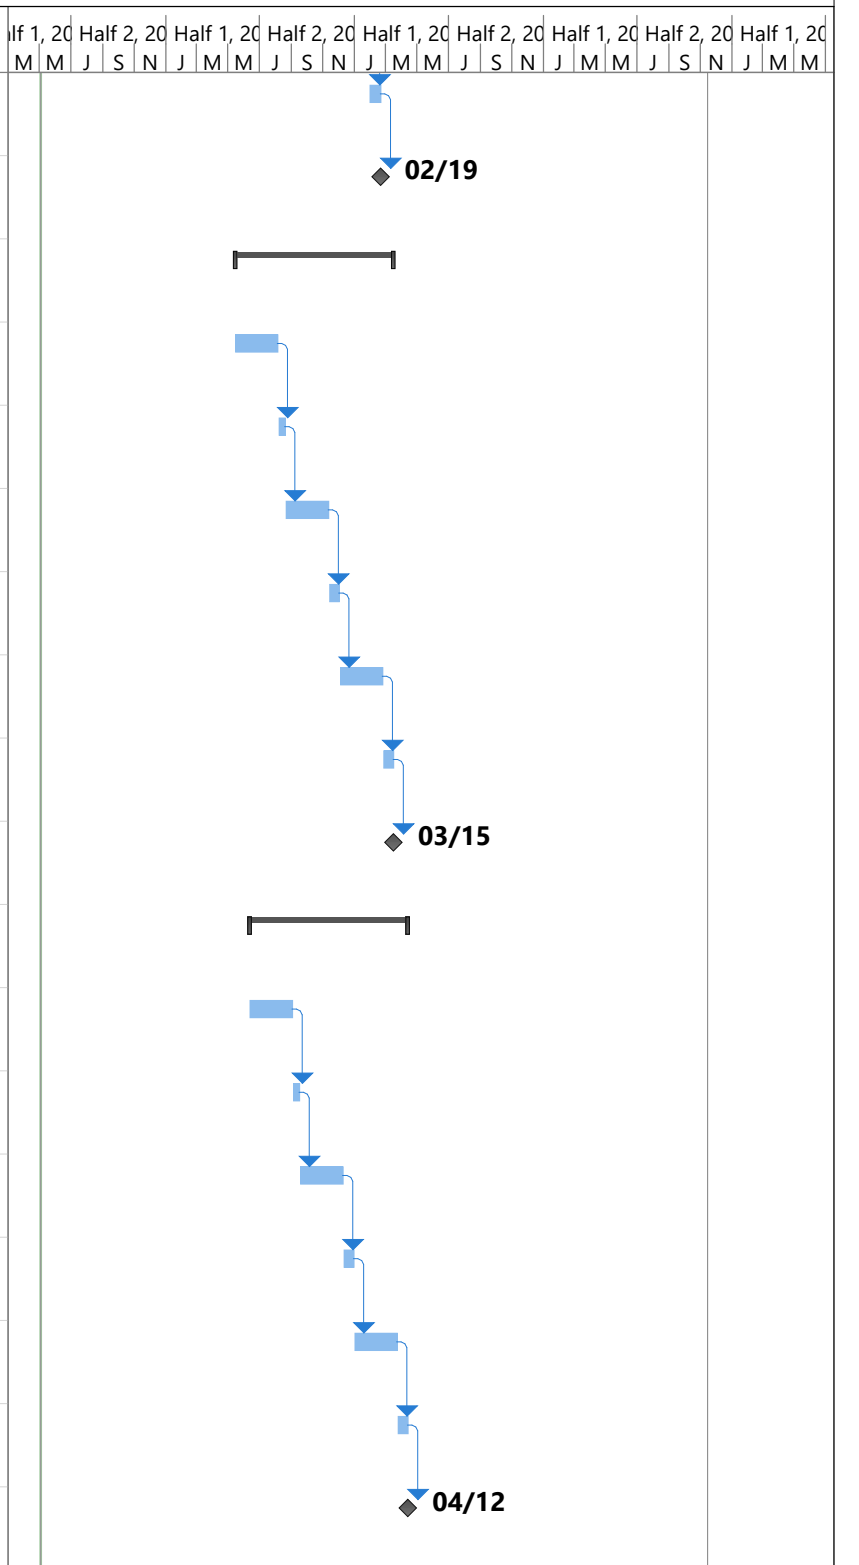


Project: 11 culverts project sche
Date: Wed 05/04/22

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Skagit County - propose schedules with RCO (11 culverts design completed by 2025)

ID	Task Name	Duration	Start	Finish	Predecessors	Notes	lf 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	
							M	M	J	S	N	J	M	M	J	S	N
49	Bulson Road - Bulson Creek (CR142)	220 days	Mon 07/10/23	Fri 05/10/24		(48.34488, -122.31261)											
50	30% Plans	3 mons	Mon 07/10/23	Fri 09/29/23													
51	30% Review; provide comments	2 wks	Mon 10/02/23	Fri 10/13/23	50												
52	60% Plans & Specs	3 mons	Mon 10/16/23	Fri 01/05/24	51												
53	60% Review; provide comments	3 wks	Mon 01/08/24	Fri 01/26/24	52												
54	90% Plans & Specs	3 mons	Mon 01/29/24	Fri 04/19/24	53												
55	90% Review; provide comments	3 wks	Mon 04/22/24	Fri 05/10/24	54												
56	Apply for Grant	0 mons	Fri 05/10/24	Fri 05/10/24	55												
57	Group 3 - Culverts (2025)	475 days	Mon 01/22/24	Fri 11/14/25													
58	Concrete Sauk Valley Rd - Rudd Creek (04.0675 0.54)	200 days	Mon 05/20/24	Fri 02/21/25		(48.45483, -121.61004)											
59	30% Plans	2 mons	Mon 05/20/24	Fri 07/12/24	55												
60	30% Review; provide comments	2 wks	Mon 07/15/24	Fri 07/26/24	59												
61	60% Plans & Specs	3 mons	Mon 07/29/24	Fri 10/18/24	60												
62	60% Review; provide comments	3 wks	Mon 10/21/24	Fri 11/08/24	61												
63	90% Plans & Specs	3 mons	Mon 11/11/24	Fri 01/31/25	62												
64	90% Review; provide comments	3 wks	Mon 02/03/25	Fri 02/21/25	63												
65	Apply for Grant	0 mons	Fri 02/21/25	Fri 02/21/25	64	FBRB											

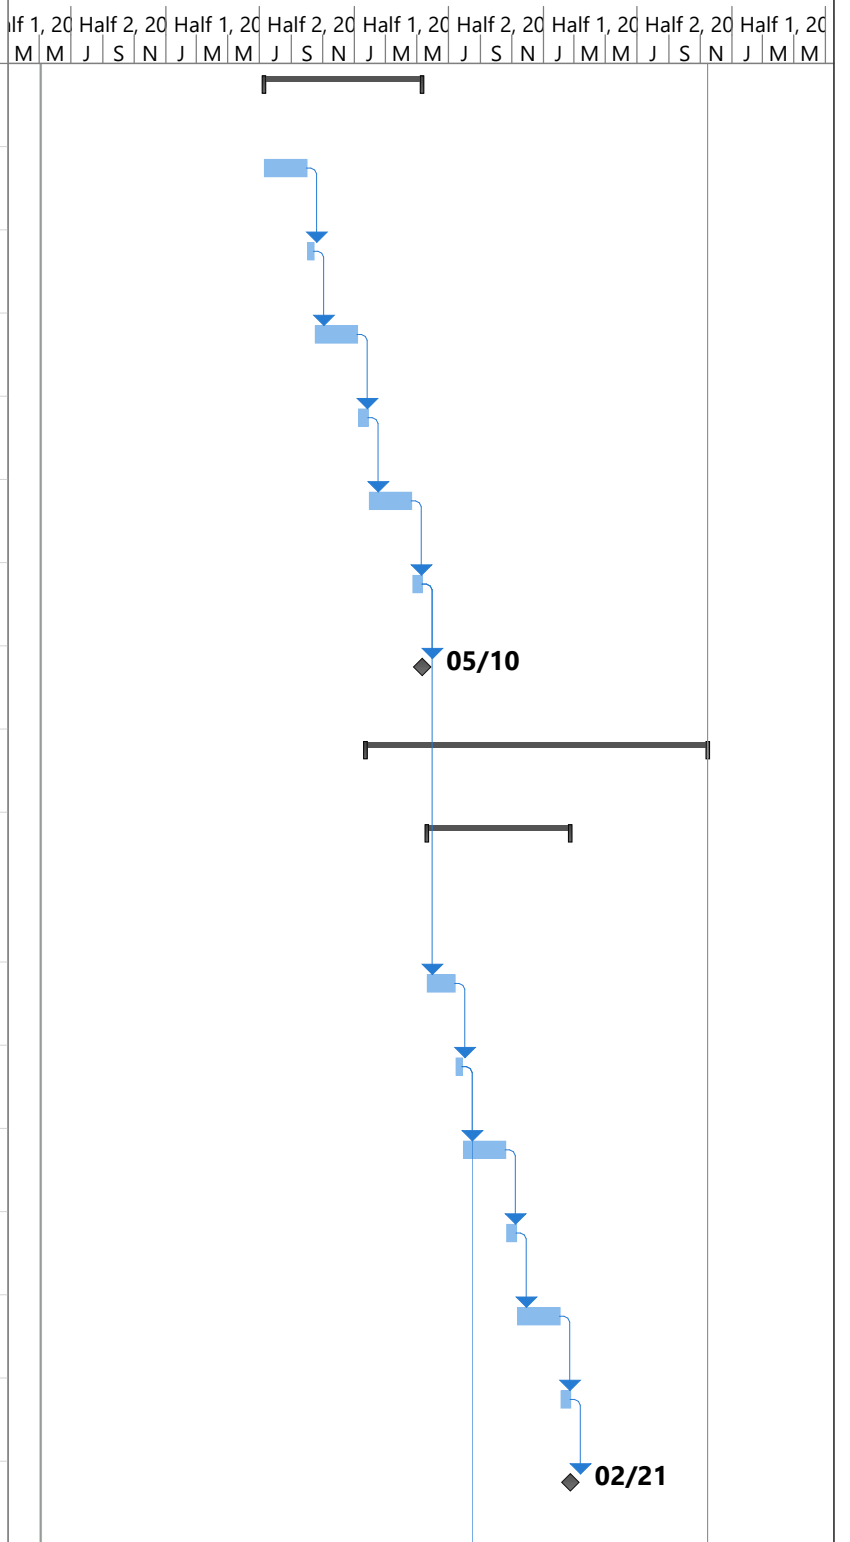


Project: 11 culverts project sche
Date: Wed 05/04/22

Task		Project Summary		Manual Task		Start-only		External Tasks		Manual Progress	
Split		Inactive Task		Duration-only		Finish-only		External Milestone		Manual Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		External Milestone		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone		External Milestone		Manual Progress	

Skagit County - propose schedules with RCO (11 culverts design completed by 2025)

ID	Task Name	Duration	Start	Finish	Predecessors	Notes	if 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20											
							M	M	J	S	N	J	M	M	J	S	N	J	M	M	J	S	N	J	M	M
66	Sauk City Road - unnamed Ck (CD 5)	200 days	Mon 07/29/24	Fri 05/02/25		(48.50122, -121.65572)																				
67	30% Plans	2 mons	Mon 07/29/24	Fri 09/20/24	60																					
68	30% Review; provide comments	2 wks	Mon 09/23/24	Fri 10/04/24	67																					
69	60% Plans & Specs	3 mons	Mon 10/07/24	Fri 12/27/24	68																					
70	60% Review; provide comments	3 wks	Mon 12/30/24	Fri 01/17/25	69																					
71	90% Plans & Specs	3 mons	Mon 01/20/25	Fri 04/11/25	70																					
72	90% Review; provide comments	3 wks	Mon 04/14/25	Fri 05/02/25	71																					
73	Apply for Grant	0 mons	Fri 05/02/25	Fri 05/02/25	72	FBRB																				
74	Sauk Store Rd - unnamed Ck (CD 6)	160 days	Mon 01/22/24	Fri 08/30/24		(48.50488, -121.6592)																				
75	30% Plans	2 mons	Mon 10/07/24	Fri 11/29/24	68																					
76	30% Review; provide comments	2 wks	Mon 12/02/24	Fri 12/13/24	75																					
77	60% Plans & Specs	3 mons	Mon 12/16/24	Fri 03/07/25	76																					
78	60% Review; provide comments	3 wks	Mon 03/10/25	Fri 03/28/25	77																					
79	90% Plans & Specs	3 mons	Mon 03/31/25	Fri 06/20/25	78																					
80	90% Review; provide comments	3 wks	Mon 06/23/25	Fri 07/11/25	79																					
81	Apply for Grant	0 mons	Fri 07/11/25	Fri 07/11/25	80	FBRB																				
82	Tyee Road - unnamed Ck (999114)	160 days	Mon 01/22/24	Fri 08/30/24		(48.31918, -122.2803)																				
83	30% Plans	2 mons	Mon 12/16/24	Fri 02/07/25	76																					

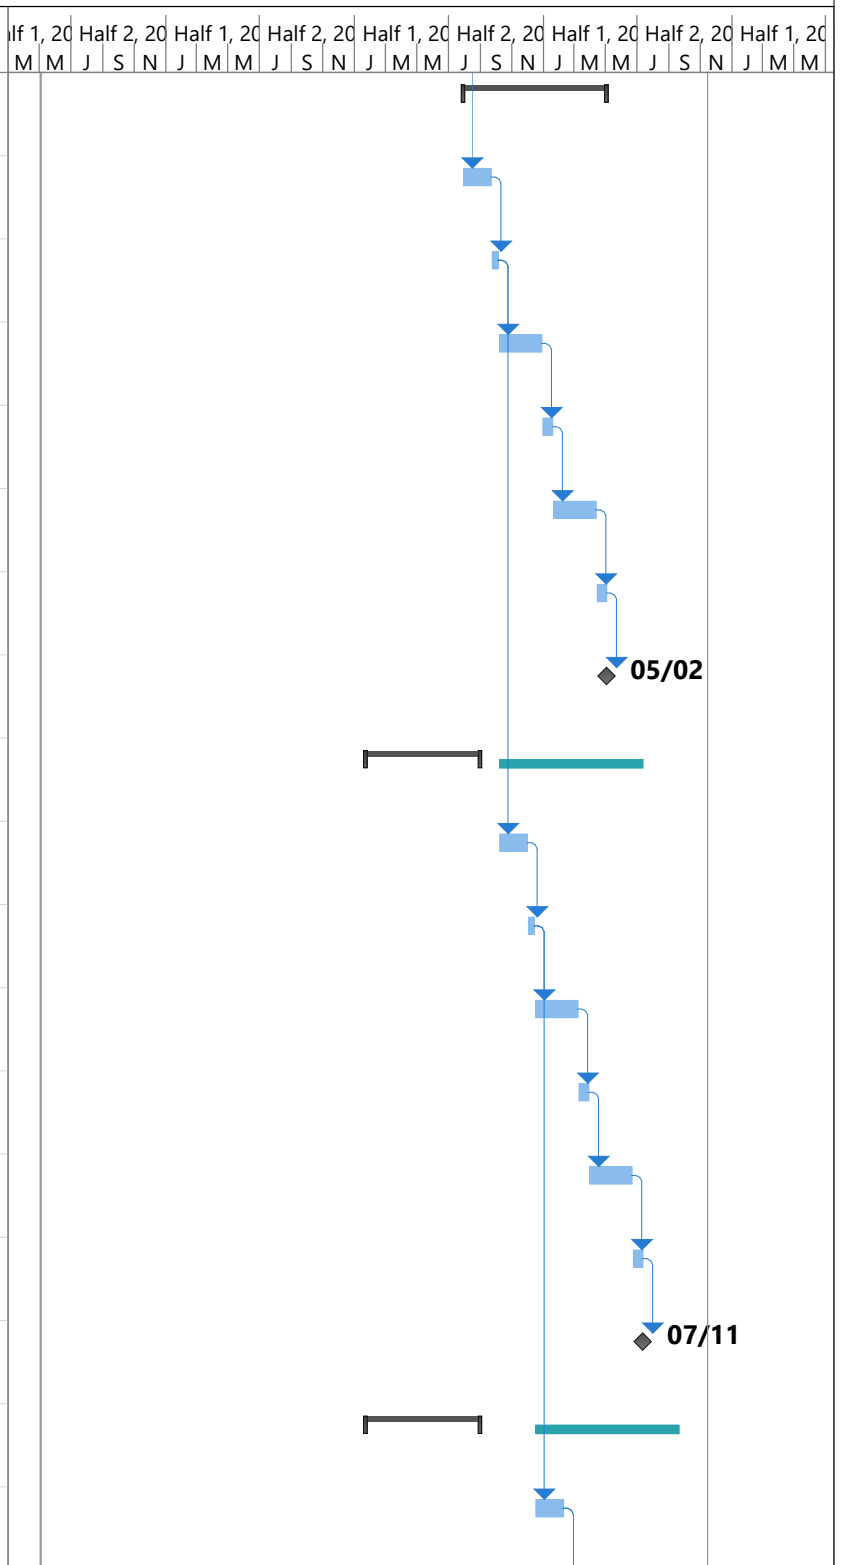


Project: 11 culverts project sche
Date: Wed 05/04/22

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Skagit County - propose schedules with RCO (11 culverts design completed by 2025)

ID	Task Name	Duration	Start	Finish	Predecessors	Notes	if 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	Half 2, 20	Half 1, 20	
							M	M	J	S	N	J	M	M	J	S	N	J
84	30% Review; provide comments	2 wks	Mon 02/10/25	Fri 02/21/25	83													
85	60% Plans & Specs	3 mons	Mon 02/24/25	Fri 05/16/25	84													
86	60% Review; provide comments	3 wks	Mon 05/19/25	Fri 06/06/25	85													
87	90% Plans & Specs	3 mons	Mon 06/09/25	Fri 08/29/25	86													
88	90% Review; provide comments	3 wks	Mon 09/01/25	Fri 09/19/25	87													
89	Apply for Grant	0 mons	Fri 09/19/25	Fri 09/19/25	88	FBRB												
90	Starbird Rd - unnamed Creek (CR80)	160 days	Mon 01/22/24	Fri 08/30/24		(48.30813, -122.27557)												
91	30% Plans	2 mons	Mon 02/10/25	Fri 04/04/25	83													
92	30% Review; provide comments	2 wks	Mon 04/07/25	Fri 04/18/25	91													
93	60% Plans & Specs	3 mons	Mon 04/21/25	Fri 07/11/25	92													
94	60% Review; provide comments	3 wks	Mon 07/14/25	Fri 08/01/25	93													
95	90% Plans & Specs	3 mons	Mon 08/04/25	Fri 10/24/25	94													
96	90% Review; provide comments	3 wks	Mon 10/27/25	Fri 11/14/25	95													
97	Apply for Grant	0 mons	Fri 11/14/25	Fri 11/14/25	96	FBRB												

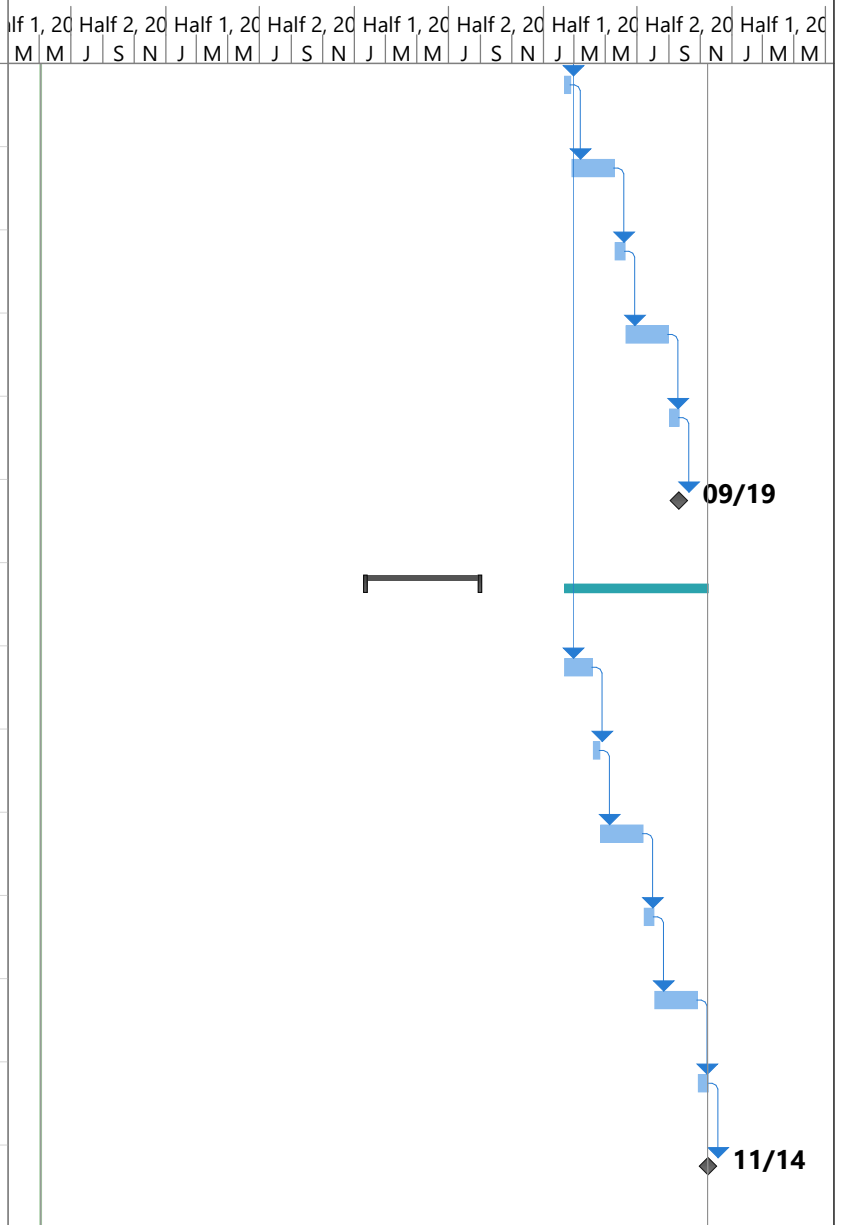

Project: 11 culverts project sche
Date: Wed 05/04/22

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			
