

Farm to Market Road / Josh Wilson Road Intersection Improvements

Project Number ES31010-4

UPDATED 7/18/2022


July 2022:

Construction has progressed well; despite the significant and unseasonable amount of rain we experienced throughout May and June. In short, yes, the rain has impacted our construction schedule. Where we originally hoped to be finishing work in early to mid-August, we are now hopeful to be finishing most construction activities by late August, with final striping to be done in September.

This month, the contractor should finally be able to complete all road and ditch grading as well as the final storm conveyance installations (a few remaining minor items). They are now working to install concrete curbing for the traffic islands, truck aprons, and central island (targeted to finish in the first week of August). Puget Sound Energy is also on the schedule this month to install the illumination pole foundations and then later next month (August), the luminaire poles.

Project Description

This project will convert an existing two-way stop-controlled intersection at Farm to Market Road and Josh Wilson Road meet into a single-lane roundabout. The work will include the construction of a central island, truck apron, concrete curb and gutter splitter islands, new stormwater culvert, new asphalt roadway surfacing, lane striping, new road signs, and the installation of an illumination system to light the intersection.

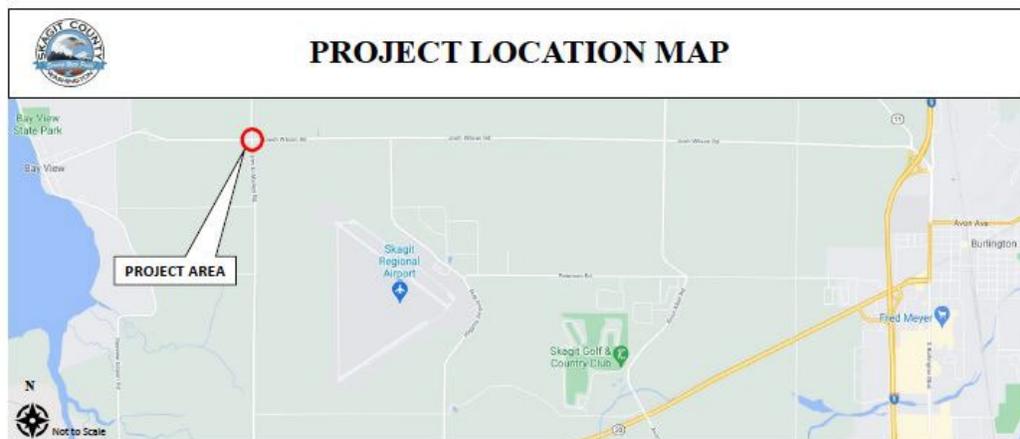

The Engineer's estimated construction cost range is between \$1.5 and 1.8M


Bids were opened on July 19th, 2021.

Contractor will begin prepping the site on September 13, 2021. The scheduled road closure will go into effect on September 20, 2021

Construction Traffic

The scheduled work for the Farm to Market Roundabout will overlap with the scheduled construction of the Josh Wilson Road – Phase 1 Project.

Detour Routes

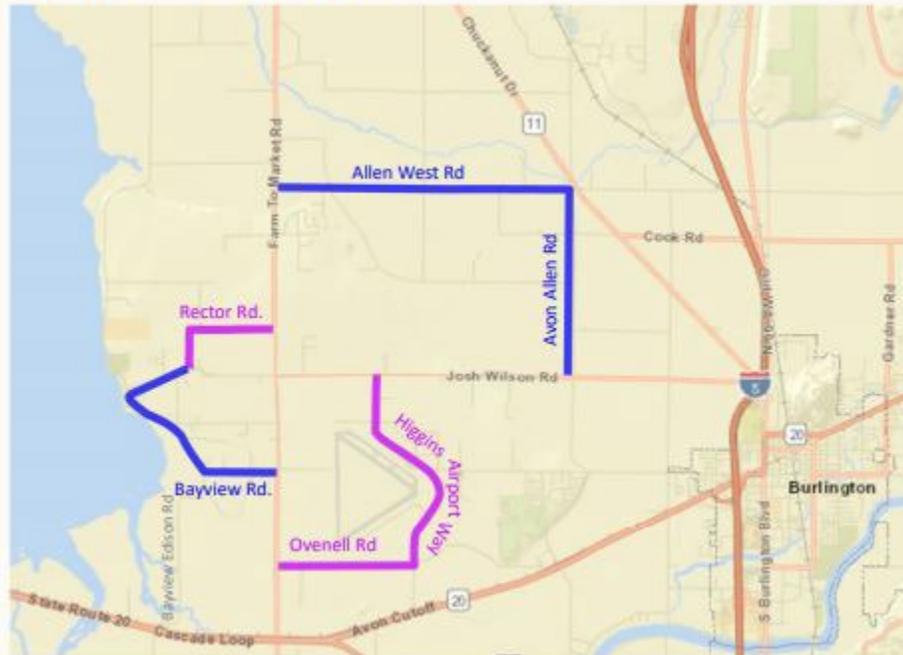

[Josh Wilson Road – Phase 1 Project and Detour information](#)

Funding Sources

- Skagit County Road Fund
- Contract was awarded to Colacurcio Brothers on July 26th, 2021 for the amount of \$1,235,177.00

For more information, contact:

Sonny Andrew – Project Manager
(360)416-1400 / sonnya@co.skagit.wa.us
